

MCHS

CONSTRUCTION PROJECT UPDATE – MAY 6, 2019



CONSTRUCTION PROJECT UPDATE

- **BUILDINGS – COMPLETED LAST 30 DAYS**

- CTE...TPO ROOF 98%. CTE MECHANICAL/ELECTRICAL/PLUMBING IN FRAMED WALLS COMPLETED. OVERHEAD ROUGH IN AT 80%. WINDOW GLAZING AT 70%. BLOCK FILL STARTED. GROUND FACED MASONRY IS 95%.
- HS...SLAB ON GRADE FOR AREA A IS COMPLETED. SLAB ON DECK IN AREA C AND E IS COMPLETE. LOAD BEARING WALLS IN AUDITORIUM ARE 95%. STAIR AND ELEVATOR TOWERS IN E/F ARE COMPLETE. EXTERIOR METAL STUDS FOR AREA C IS COMPLETE. STRUCTURAL STEEL IN AREA E IS COMPLETE. ROOF TRUSS AND DECKING IN GYM/AUXILIARY GYM COMPLETE. EXCESS SOIL RELOCATION IS COMPLETE.

CONSTRUCTION PROJECT UPDATE

- **NEXT 30 DAYS**

- CTE – CONTINUE TO POLISH GROUND FACED BLOCK. PREPARE/CLEAN CMU BLOCK FOR FILLER. CONTINUE OVERHEAD MEP ROUGH IN. BEGIN ROOF TRIM METAL. MOUNT ROOFTOP MECHANICAL UNITS.
- HS – INTERIOR METAL STUDS IN AREA C. ERECT STRUCTURAL STEEL FOR AREA F. BEGIN STEEL FRAMING MECHANICAL AREAS. ERECT CMU CORRIDOR WALLS IN AREA E/F.
- SITE – FOOTINGS FOR 3 OF 11 BUILDING HAVE BEEN POURED, BEGIN ERECTING FOUNDATION BLOCK. FINE GRADE OF GLENN ROAD CONNECTOR. POUR SLAB ON DECK IN AREA F.
- NEXT PROGRESS MEETING IS SCHEDULED FOR JUNE 6, 2019 (ANOTHER ACADEMIC YEAR DOWN!).



BRANCH

BRANCH
CIVIL

STEEL SUPPLY & ERECTION CO., INC.
ASHEBORO, NC
336 - 625 - 4830

BUTNER
CONSTRUCTION

ACE Electric, Inc.
ELECTRICAL AND COMMUNICATIONS CONTRACTORS

Fire Sprinkler
Service, LLC

CTE SUBSTANTIAL COMPLETION DATE – 10/31/2019

MCHS SUBSTANTIAL COMPLETION DATE – 3/11/2020

Chandler inc.

BLANCHET CONCRETE
PUMPING, L.L.C.

05/01/2019

05/01/2019

MW
MECHWORKS
MECHANICAL CONTRACTORS, INC.
www.mechworksinc.com

PROFESSIONAL
DRYWALL, LLC
FRAMING, DRYWALL &
ACOUSTICAL CEILINGS
336-893-7152

SPC
MECHANICAL
www.SPCmechanical.com



East Face of Instructional Wing



Facing Southwest across student parking lot



Main drive to Glenn Road – note placed soil in rear



Visitors Steps and Home Bleacher Area



View Southwest from Visitor Steps




Football field with Running Track rough grade



05/01/20

Finally – clear enough to pour the Boys Locker Room


KEY PLAN

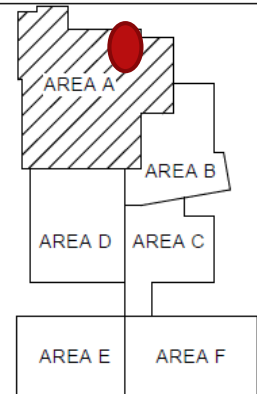



ROTC floor in progress


KEY PLAN

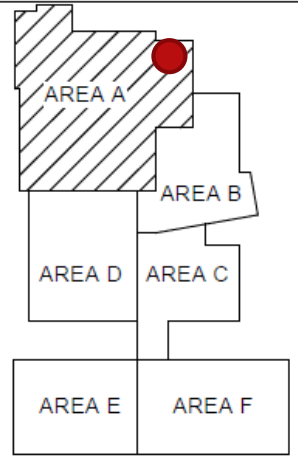



Facing South down Main Corridor


KEY PLAN

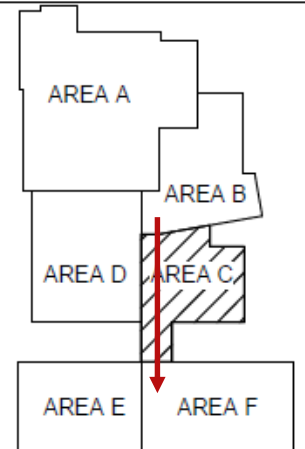



North and East Walls of Office and Media Center.


KEY PLAN

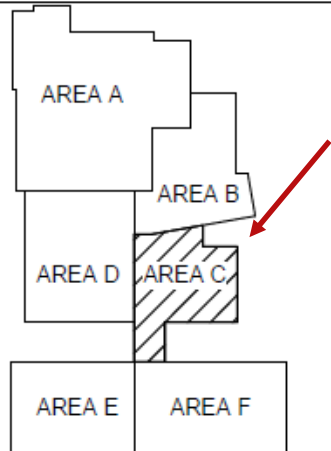



South and East Walls of Office and Media Center


KEY PLAN

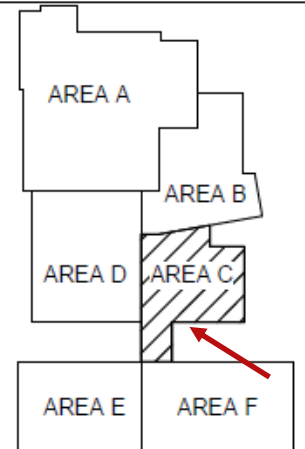



West Face of Gym, Auditorium and Band Room


KEY PLAN

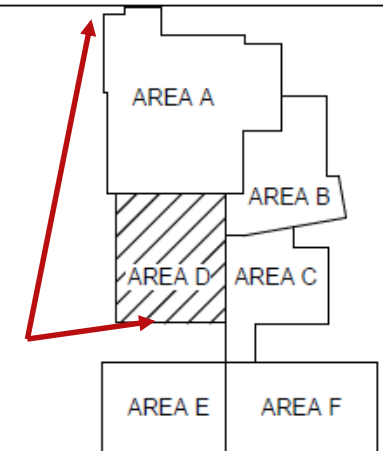



05/02/20


Mechanical Room, Weight Room and Auxiliary Gym

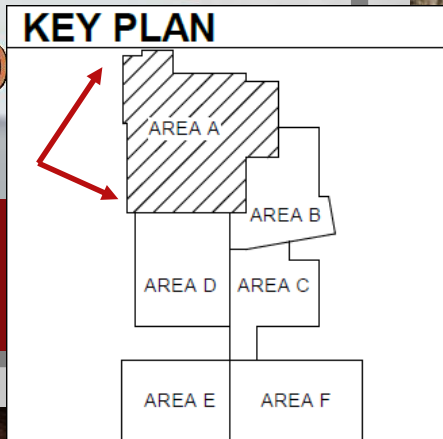



Auditorium, Band Room, Courtyard, Area E


KEY PLAN

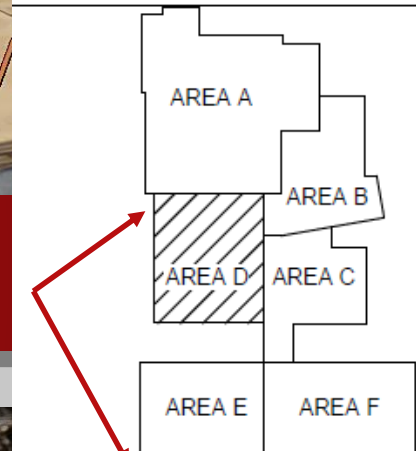



South Face of Band, Chorus, Dance and Drama


KEY PLAN

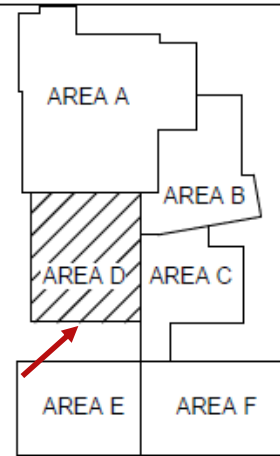



Art Room in Area E


KEY PLAN

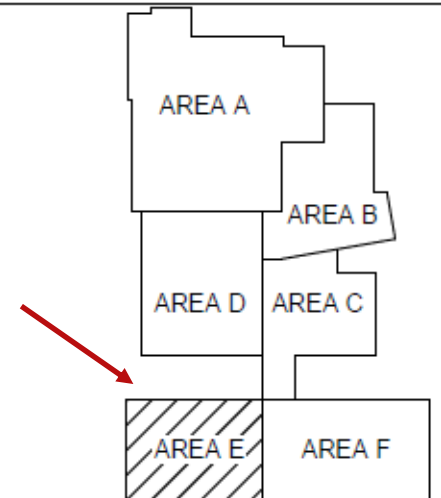



Facing East down Classroom Wing Area E


KEY PLAN

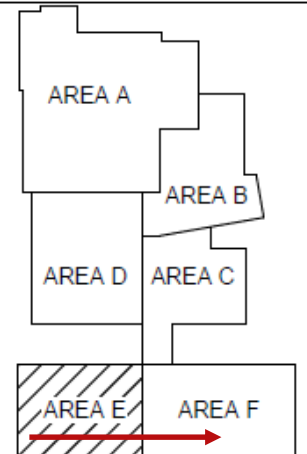



2nd Floor Area E ready for pour


KEY PLAN

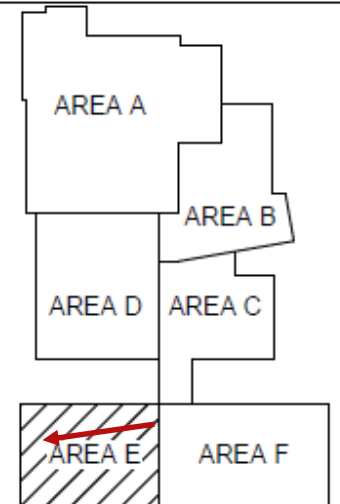



Area F Structural Steel in Progress


KEY PLAN

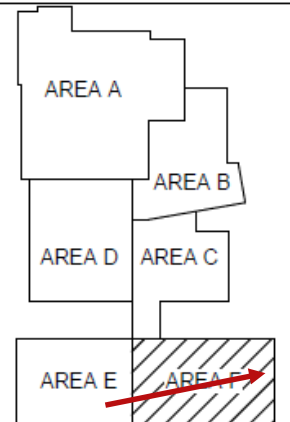



CTE Building East and South Face


KEY PLAN













TPO roof in progress – CTE Building

KEY PLAN





END SLIDE – QUESTIONS???

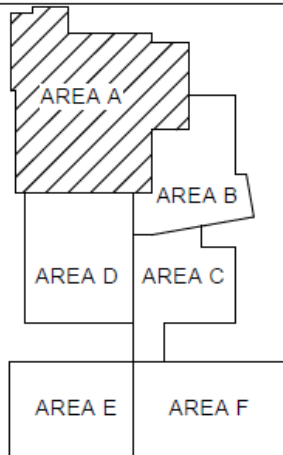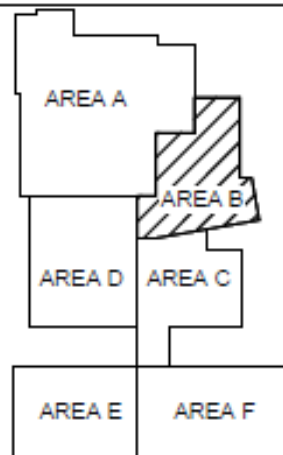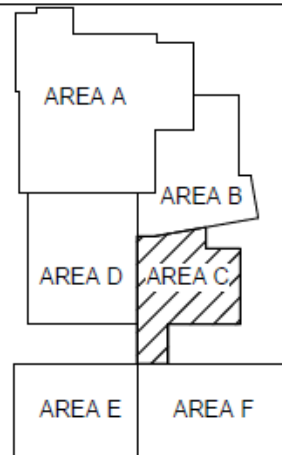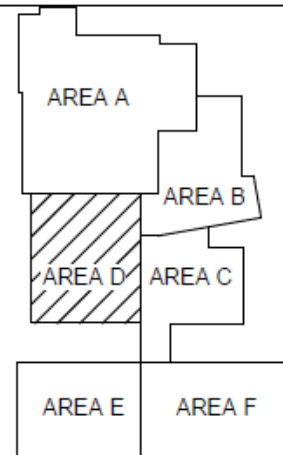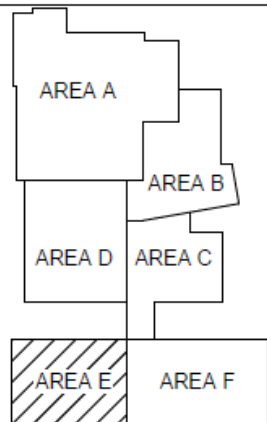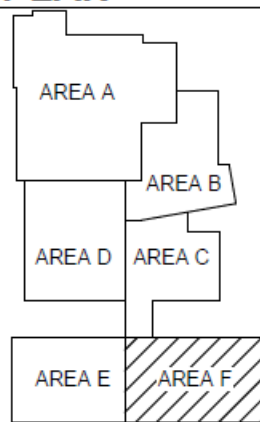KEY PLAN**KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN**

KEY BLOCK – DO NOT DELETE
