

MCHS

CONSTRUCTION PROJECT UPDATE – SEPTEMBER 9, 2019



CONSTRUCTION PROJECT UPDATE

- **BUILDINGS – COMPLETED LAST 30 DAYS**

- CTE...HVAC HAS STARTED, GAS TANK SET FOR MAIN BOILER START. CEILING GRID IS 99%. OVERHEAD INSPECTIONS COMPLETED. VCT FLOOR PREP STARTED. OVERHEAD MEP ONGOING. SIDEWALKS HAVE STARTED. TOPSOIL IS ONGOING. DUST COLLECTOR PIPING IS 90%. WELDING AIR SCRUBBERS ARE SET.
- HS...TPO ROOF ON AREAS A1, D, E AND F COMPLETED. MEP ROUGH IN OF AREA A1 AT 95%. MECHANICAL MEZZANINE IN ARE B POURED AND UNITS SET. STONE BASE OF ROADWAY TO GLENN STREET AND STUDENT PARKING IS ON-GOING (CARRY OVER). CURB AROUND TRACK IS 95% COMPLETE. CMU AT STADIUM RESTROOMS IS COMPLETE. COMMUNICATION PATHWAYS TO OUTBUILDINGS IS COMPLETE.

CONSTRUCTION PROJECT UPDATE

- **NEXT 30 DAYS**

- CTE –CONTINUE INSTALLING VCT. START BOILERS FOR DEHUMIDIFICATION. BEGIN CEILING TILE PLACEMENT. CONTINUE INSTALLING VCT FLOORING. BEGIN CASEWORK. CONTINUE FINAL PAINTING. FINISH OVERHEAD LIGHTS, HOSE REELS, ELECTRICAL REELS, LOW VOLTAGE CABLING. CONTINUE WORK IN DATA CLOSETS. SEAL CONCRETE FLOORS. CONTINUE SIDEWALKS. BEGIN LANDSCAPING.
- HS –CONTINUE IN WALL AND OVERHEAD MEP ON 1ST AND 2ND LEVELS OF C, E, F. OVERHEAD ROUGH IN IN AREA D BEGINS TODAY, ALL TRADES, SCAFFOLD ERECTED. BEGIN SHEETROCK IN AREA C.
- SITE –CONTINUE STONE PLACEMENT, PAVING TO BEGIN SOON. PLACE TOPSOIL AT BASEBALL –SOFTBALL FIELDS. IRRIGATION TO FOLLOW. CONTINUE INSTALLING MAIN POWER LINE FROM CTE TO HS. MEP AT OUTBUILDING ONGOING.
- NEXT PROGRESS MEETING IS SCHEDULED FOR OCTOBER 3, 2019.



CTE SUBSTANTIAL COMPLETION DATE – 11/05/2019

MCHS SUBSTANTIAL COMPLETION DATE – 3/24/2020


Next Meeting Date 10/3/2019





Work In Progress:
Window Glazing
Exterior Weatherproofing
Brick Veneer

KEY PLAN

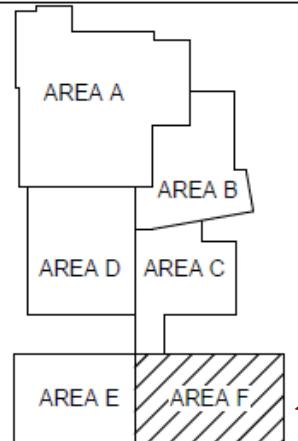


East Face of Area C and Area F



Work In Progress:
Exterior Sheathing
Window Glazing
Grout Pumping
Brick Veneer

KEY PLAN

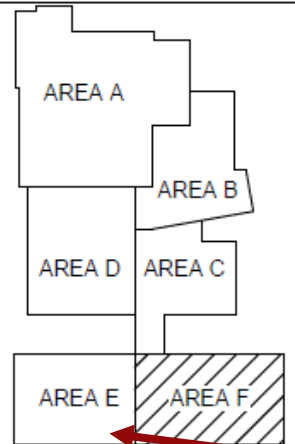


South Face of Area F – Arrow is Main Entrance



**Work In Progress:
Brick Veneer
Window Glazing**

KEY PLAN

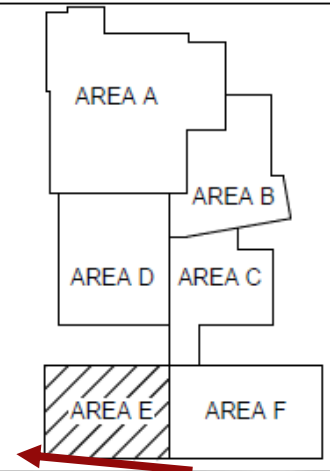


South Face of Area E – Arrow is Main Entrance



Work In Progress:
Brick cleaning
Glazing frame installation

KEY PLAN

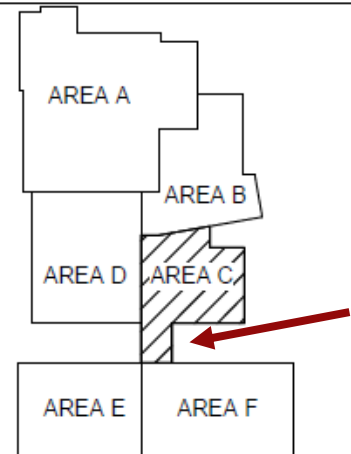


Instructional Wing Connector



Work In Progress:
Erecting Auditorium Scaffold for
ceiling access by 8 trades,
scheduled for the next 7 weeks

KEY PLAN

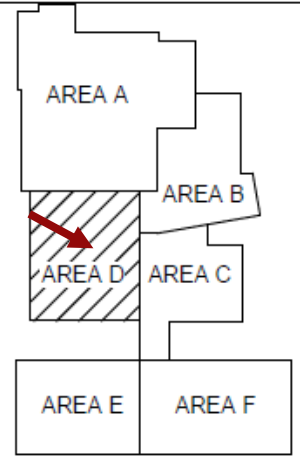


Auditorium Scaffold from Main Stage



Overhead work in Area A1

Work In Progress:
Overhead work in Area A1 has been prioritized as most of the mechanical systems originate from main mechanical room.


KEY PLAN

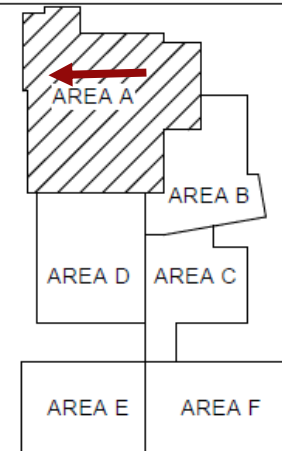



Main Mechanical Room Pipe being Fabricated


KEY PLAN

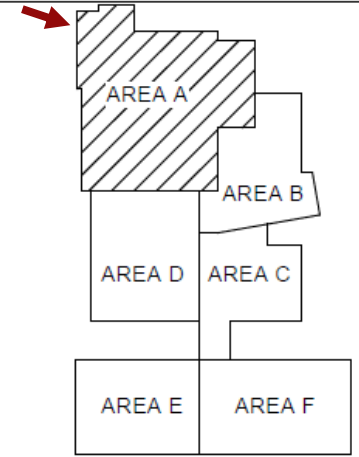



Work In Progress:
Grading main parking lot
Installation of coping metal on A

KEY PLAN

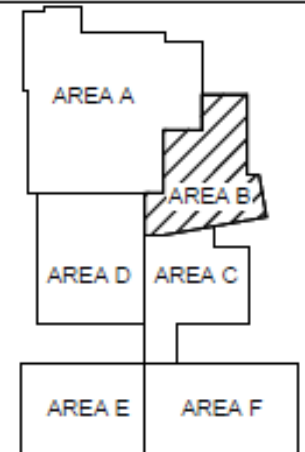

View of MCHS from Main Parking Lot



**Work In Progress:
Framing of curb gutter in main lot**

Framing of curb gutter in Main Parking Lot



Work In Progress:
Electrical installation on Announcer
Booth
Grading of Boys Baseball Field

Boys Baseball and Girls Softball Field



Football Field and Running Track




**Work In Progress:
Concession stand exterior wall
Running Track Border**

Home Side Bleacher Area – Future Field House Pad



Work In Progress:
Roof coping metal
Concrete Sidewalks

KEY PLAN

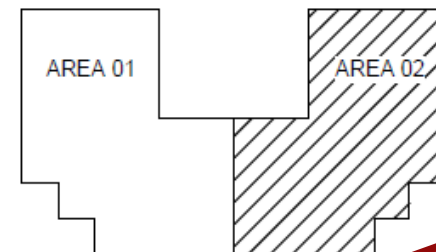


Southeast Face of CTE



Work In Progress:
Grading of main courtyard
Placing topsoil
Concrete walkway

KEY PLAN




CTE Main Courtyard



Work In Progress:
Setting Gas Tank Pads
Work in mechanical room

KEY PLAN




West Face of CTE – Mechanical Yard



**Work In Progress:
Forming for Curb Gutter
Grading Access Road**

KEY PLAN




Main Access Road CTE Rear Courtyard



**Work in Progress:
Installation of metal finish on
rear canopy**

KEY PLAN

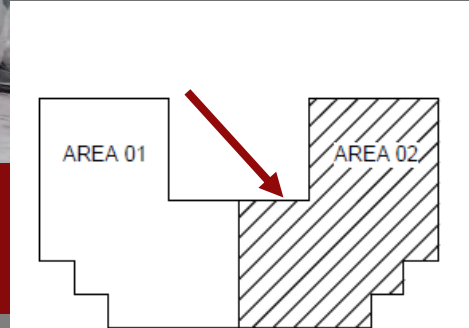

CTE Rear Courtyard Canopy



Welding Lab




Automotive Lab



Work In Progress:
Electrical – Electrical Reels,
Lights
Plumbing – Hose Reels
Mechanical – Air Scrubber

KEY PLAN




Construction Trades Lab



Wood Working Lab

Work In Progress:
Mechanical – Dust Collector
Electrical – Main Panels, outlets

KEY PLAN





Work In Progress:
Mason – Fire wall around
elevator

KEY PLAN




Main Elevator Second Floor



Work In Progress:
Floor patch in preparation of VCT
Flooring
Window Glazing









KEY PLAN



Main Hall Second Floor Area 2



END SLIDE – QUESTIONS???

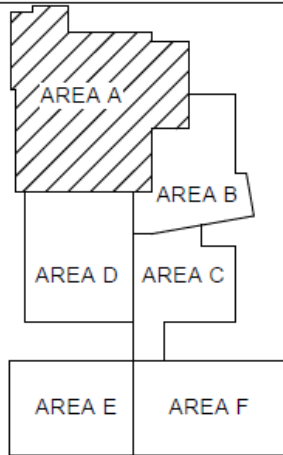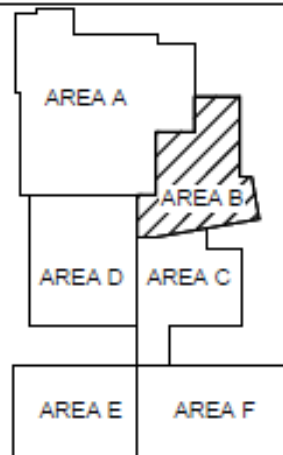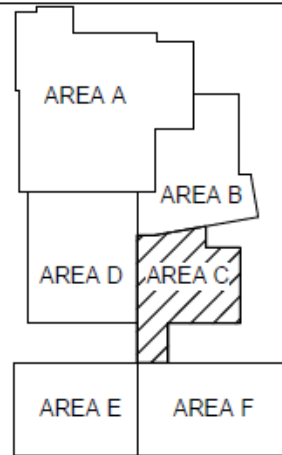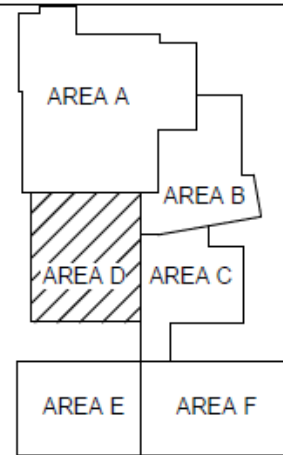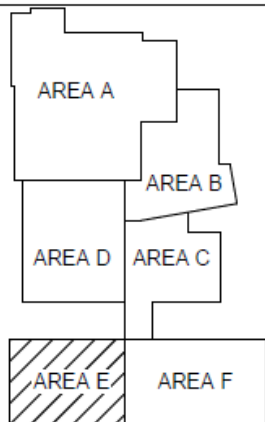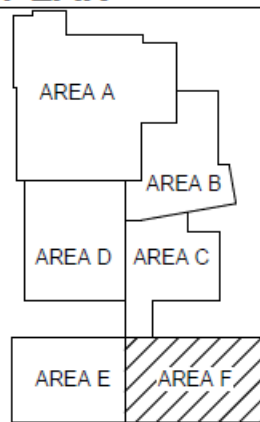KEY PLAN**KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN**

KEY BLOCK – DO NOT DELETE
