

# **MCHS**

**CONSTRUCTION PROJECT UPDATE – JUNE 3, 2019**



# CONSTRUCTION PROJECT UPDATE

- **BUILDINGS – COMPLETED LAST 30 DAYS**

- CTE...TPO ROOF MEMBRANE IS COMPLETE. METAL IS PENDING. WALL BOARD IS HAS BEEN INSTALLED ON LITE GAUGE METAL WALLS. WINDOW GLAZING IS AT 90%. WEST STAIRWELL STEPS HAVE BEEN POURED. EAST STAIRWELL STEPS ARE ROUGHED IN. CMU BLOCK FILL IS IN PROGRESS. METAL ROLL UP DOORS HAVE BEEN INSTALLED.
- HS...TPO ROOF ON GYMS IS AT 90%. EXTERIOR SHEATHING FOR AREA C COMPLETED, BRICK IN PROGRESS. AUDITORIUM TRUSSES ARE AT 95%. TRUSSES ARE COMPLETE ON LOCKER ROOMS. STRUCTURAL STEEL IN AREA F IS COMPLETE. CMU WALLS FIRST FLOOR AREA E ARE COMPLETE. CMU WALLS FIRST FLOOR AREA F ARE IN PROGRESS. CMU WALLS SECOND FLOOR AREA E ARE IN PROGRESS. METAL DECK FOR AREA F SECOND FLOOR IS IN PROGRESS.

# CONSTRUCTION PROJECT UPDATE

- **NEXT 30 DAYS**

- CTE – BEGIN ROOF TRIM METAL (CARRIED OVER). CONTINUE MEP ROUGH IN WORK. CONTINUE FINISHING WALLBOARD. CONTINUE FINISHES FOR CMU. COMPLETE GLAZING.
- HS – INTERIOR METAL STUDS IN AREA E/F. CONTINUE MEP ROUGH INS FOR AREAS E/F. CONTINUE TO ERECT CMU CORRIDOR WALLS IN AREA E/F.
- SITE –CONTINUE TO GRADING ROADWAYS AND PARKING LOTS.
- NEXT PROGRESS MEETING IS SCHEDULED FOR JUNE 6, 2019 (ANOTHER ACADEMIC YEAR DOWN!).





**CTE SUBSTANTIAL COMPLETION DATE – 10/31/2019**

**MCHS SUBSTANTIAL COMPLETION DATE – 3/11/2020**

**NO UPDATE FROM LAST MONTH. UPDATE AVAILABLE  
AFTER JUNE 6<sup>th</sup> SITE MEETING.**






05/29/2019

South Face of Instructional Wing Area E

#### KEY PLAN

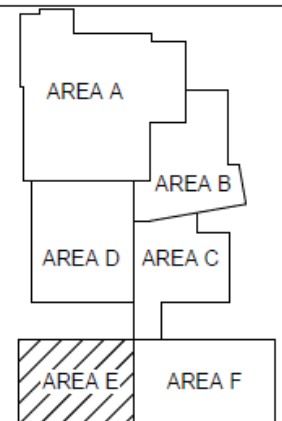






05/29/2019

South Face of Instruction Wing Area F – Chemistry Rooms

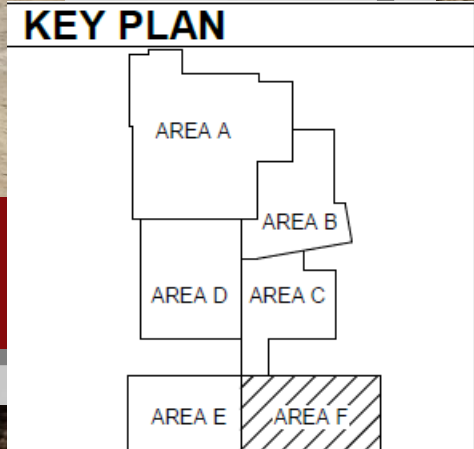






South-East Face of Area C – Office/Media

#### KEY PLAN

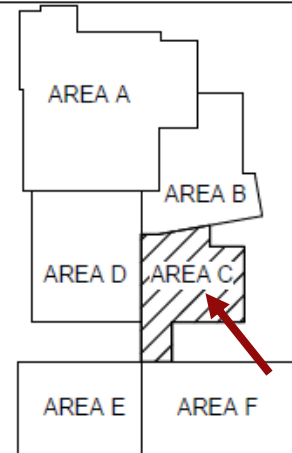






Rooftop Deck of Area D Performing Arts/Dance/Band

#### KEY PLAN

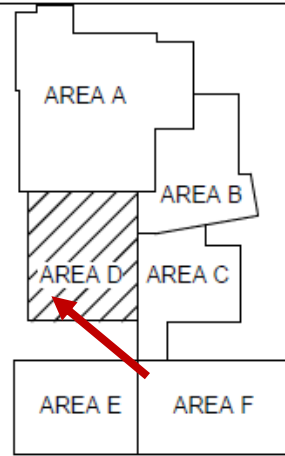






North Face of Area E – Art Room/Classrooms

KEY PLAN

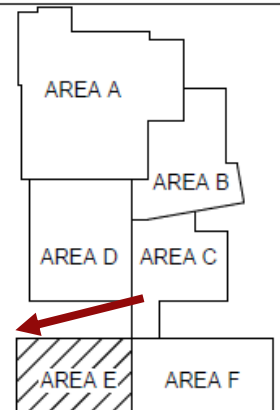






North Face of Area F – Instructional Wing

**KEY PLAN**

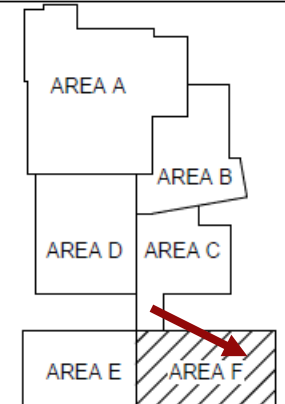






Visitor Parking Lot – Main Front Drive Loop

#### KEY PLAN

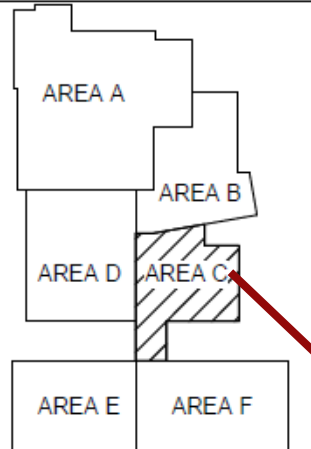






Student Parking Lot – Main Drive Loop

KEY PLAN

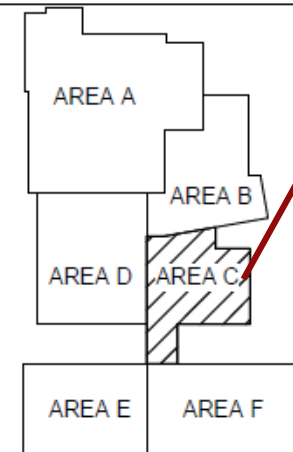





South – East Faces of CTE Building

KEY PLAN








Facing South down Main Corridor

#### KEY PLAN

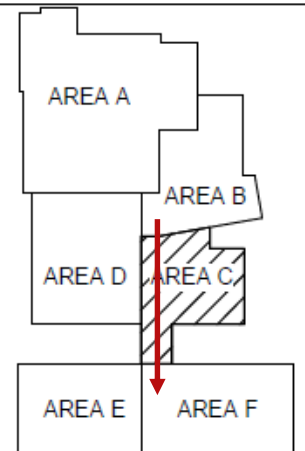






CTE through Stage Window

#### KEY PLAN

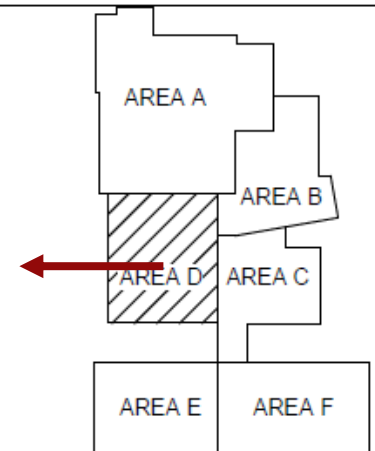













East Stairwell of CTE – Potential Logo Location?





END SLIDE – QUESTIONS???

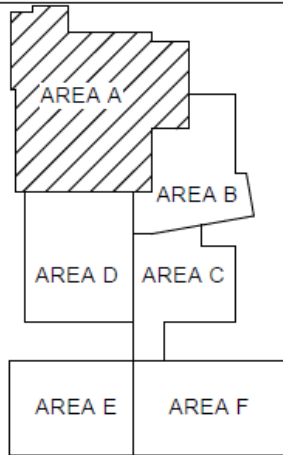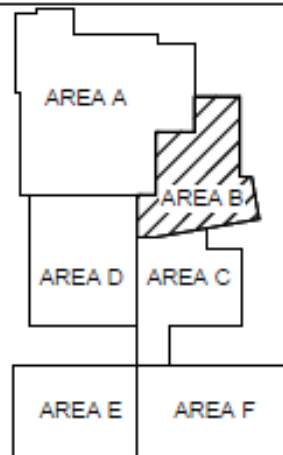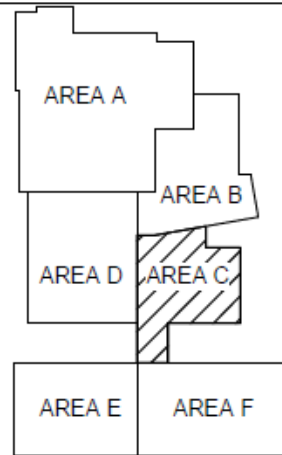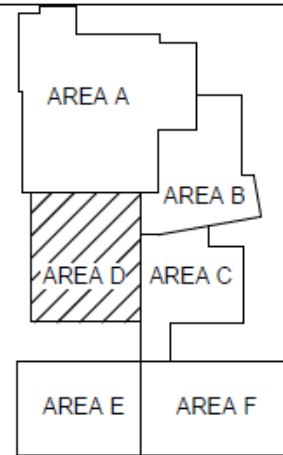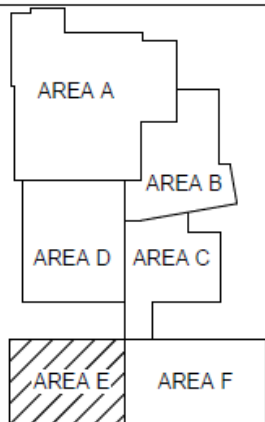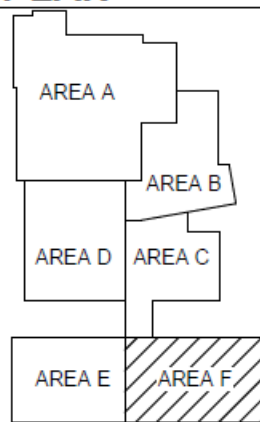

**KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN**

**KEY BLOCK – DO NOT DELETE**
