

MCHS

Construction Project Update – March 4, 2019

Construction Project Update

- Buildings
 - CTE...Interior first floor CMU walls to 97%. Second floor Slab on Deck (SOD) is complete. CMU to bearing plates in Area 1 Second Floor is complete, mechanical equipment and roof trusses in progress. CMU to bearing plates in Area 2 Second Floor is in progress.
 - CTE...Rain and cold continue to cause delays for project. Updated schedules to be presented at the next monthly meeting. Carried Over.
 - HS...CMU work is continuing in Performing Arts, including Auditorium, and the stair wells for the instructional wing. Concrete was poured for Office Area "C". Slab forming work is in progress for the instructional wing.
 - HS...the high school has also suffered weather related delays this last month. Carried Over.

Construction Project Update

- Next 30 days
 - Pour concrete slab for Instructional Wing and Dining Room.
 - Complete Exterior Brick on CTE, move onto High School Walls after spray foam is applied.
 - Finish roof trussed on CTE and Main Gym. Begin to set structural steel for office and instructional wing. Begin roof on CTE building.
 - Next Progress Meeting is scheduled for March 7, 2019.

South and East Walls of the CTE building,
front brick in progress.




North and East Walls of Courtyard,
roof truss in progress



West Wall CTE – Wood working – Agri-Science



Construction Trades – Mezzanine stairs in construction

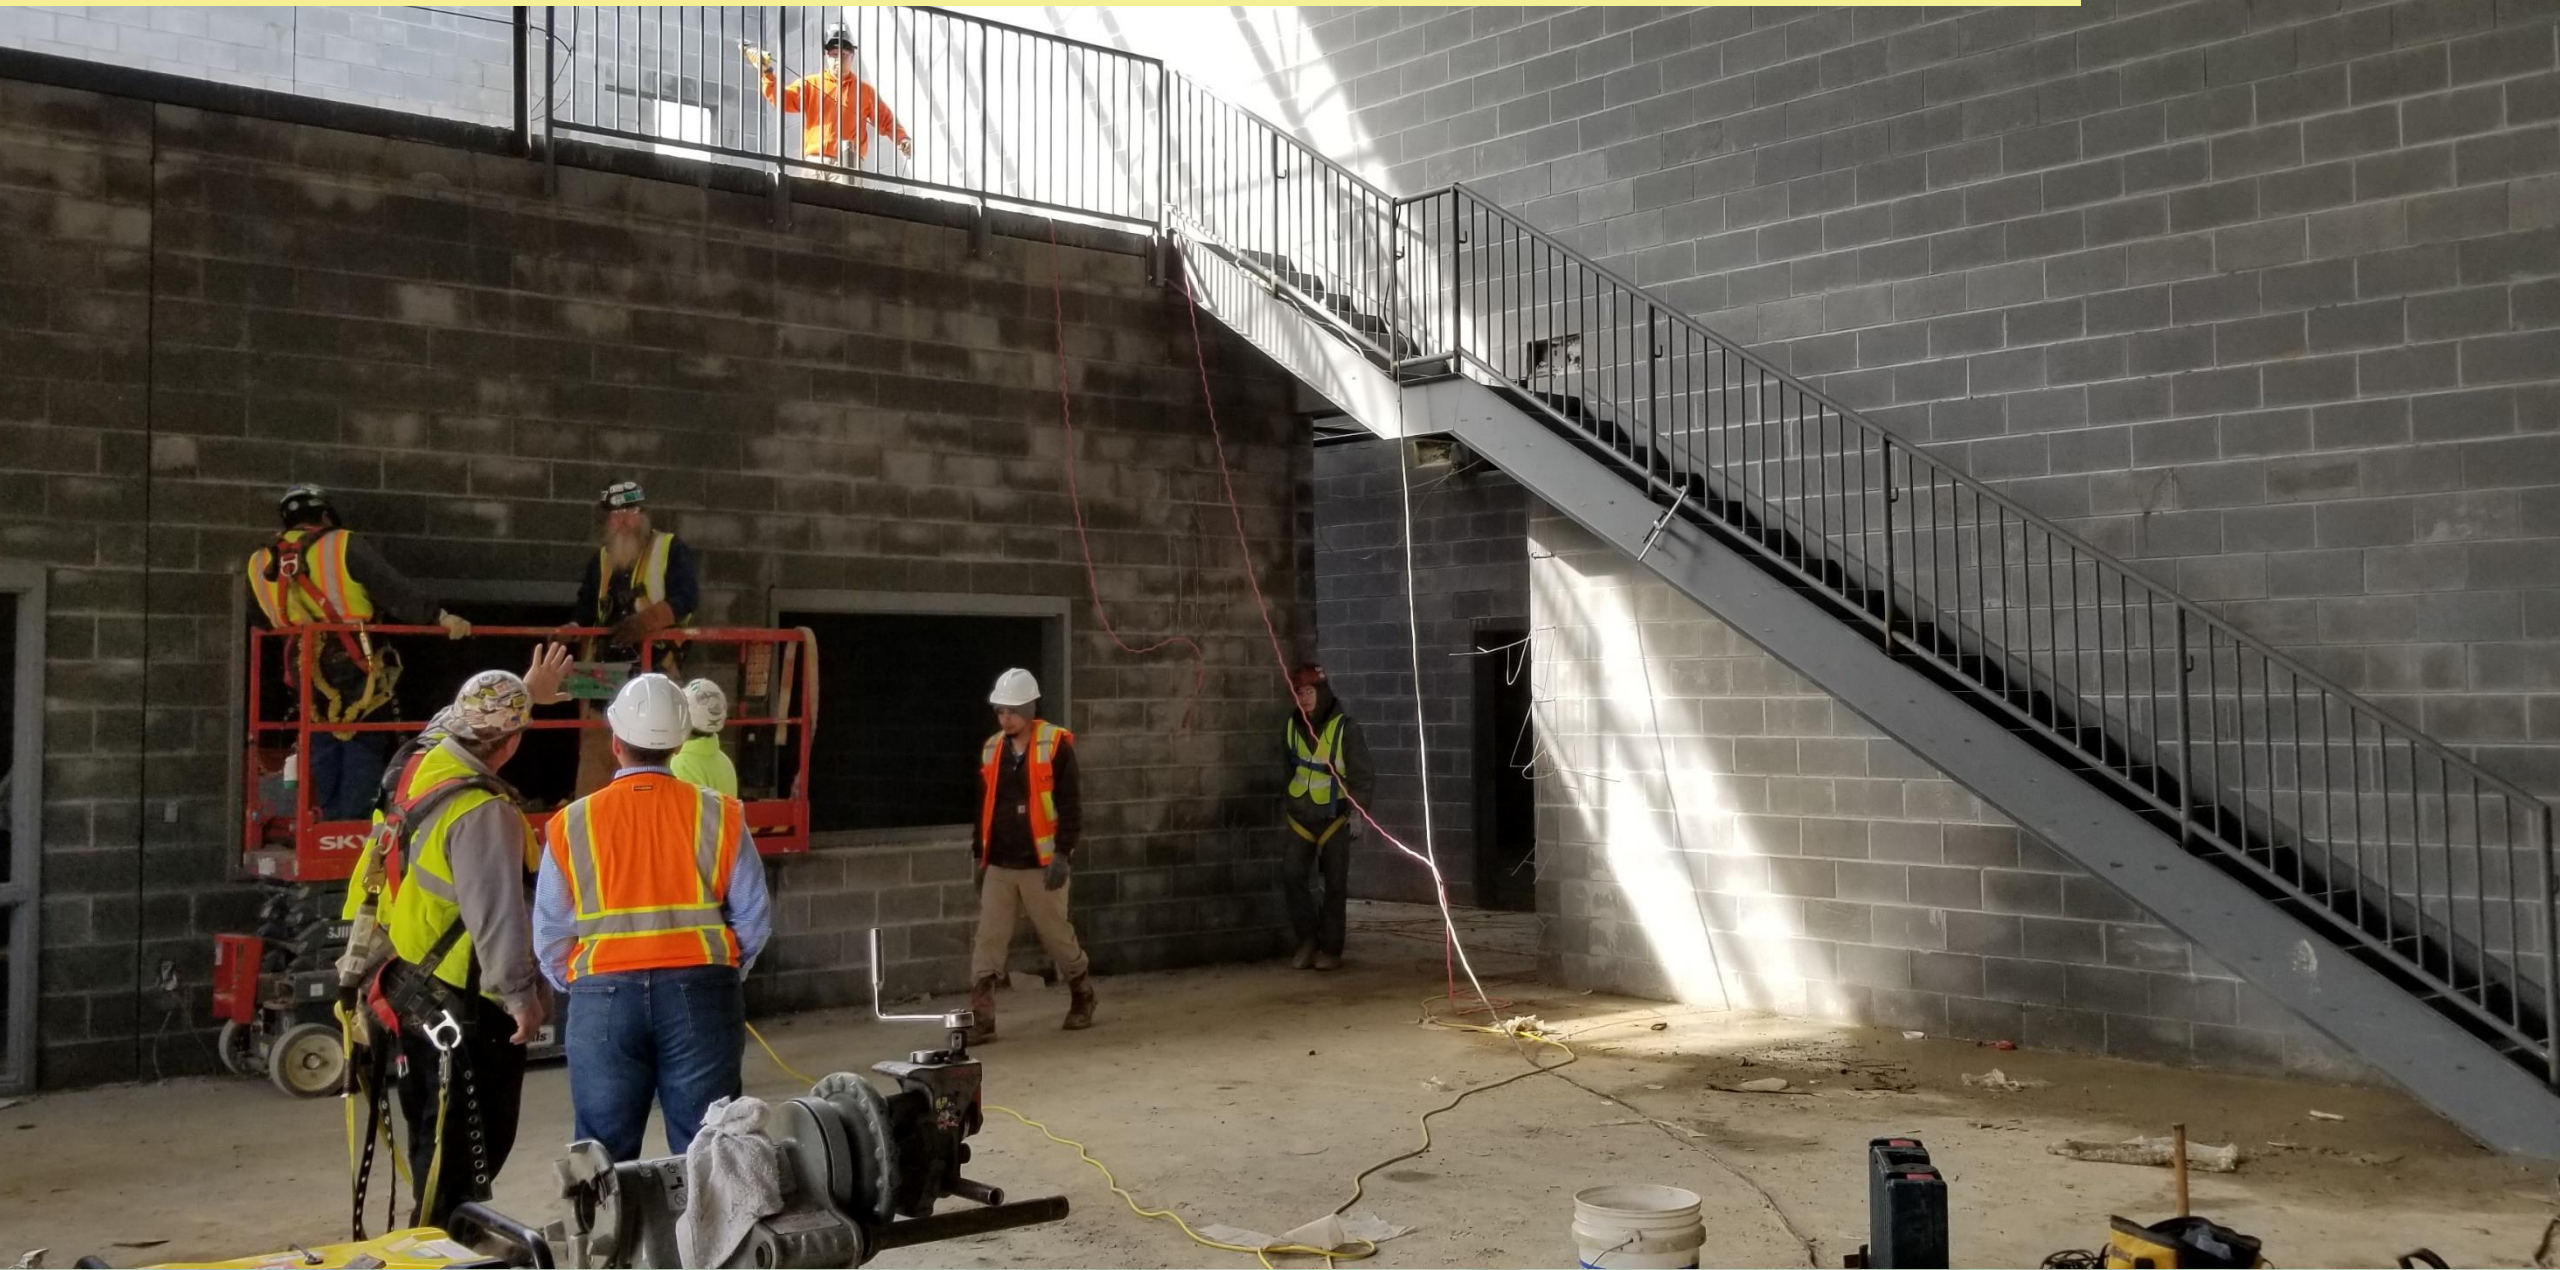

CTE Second Floor – CMU to bearing plates in progress




View from CTE Welding Mezzanine



View across office area. Note ground face CMU in Auditorium.



Auditorium from main stage – note ground face CMU

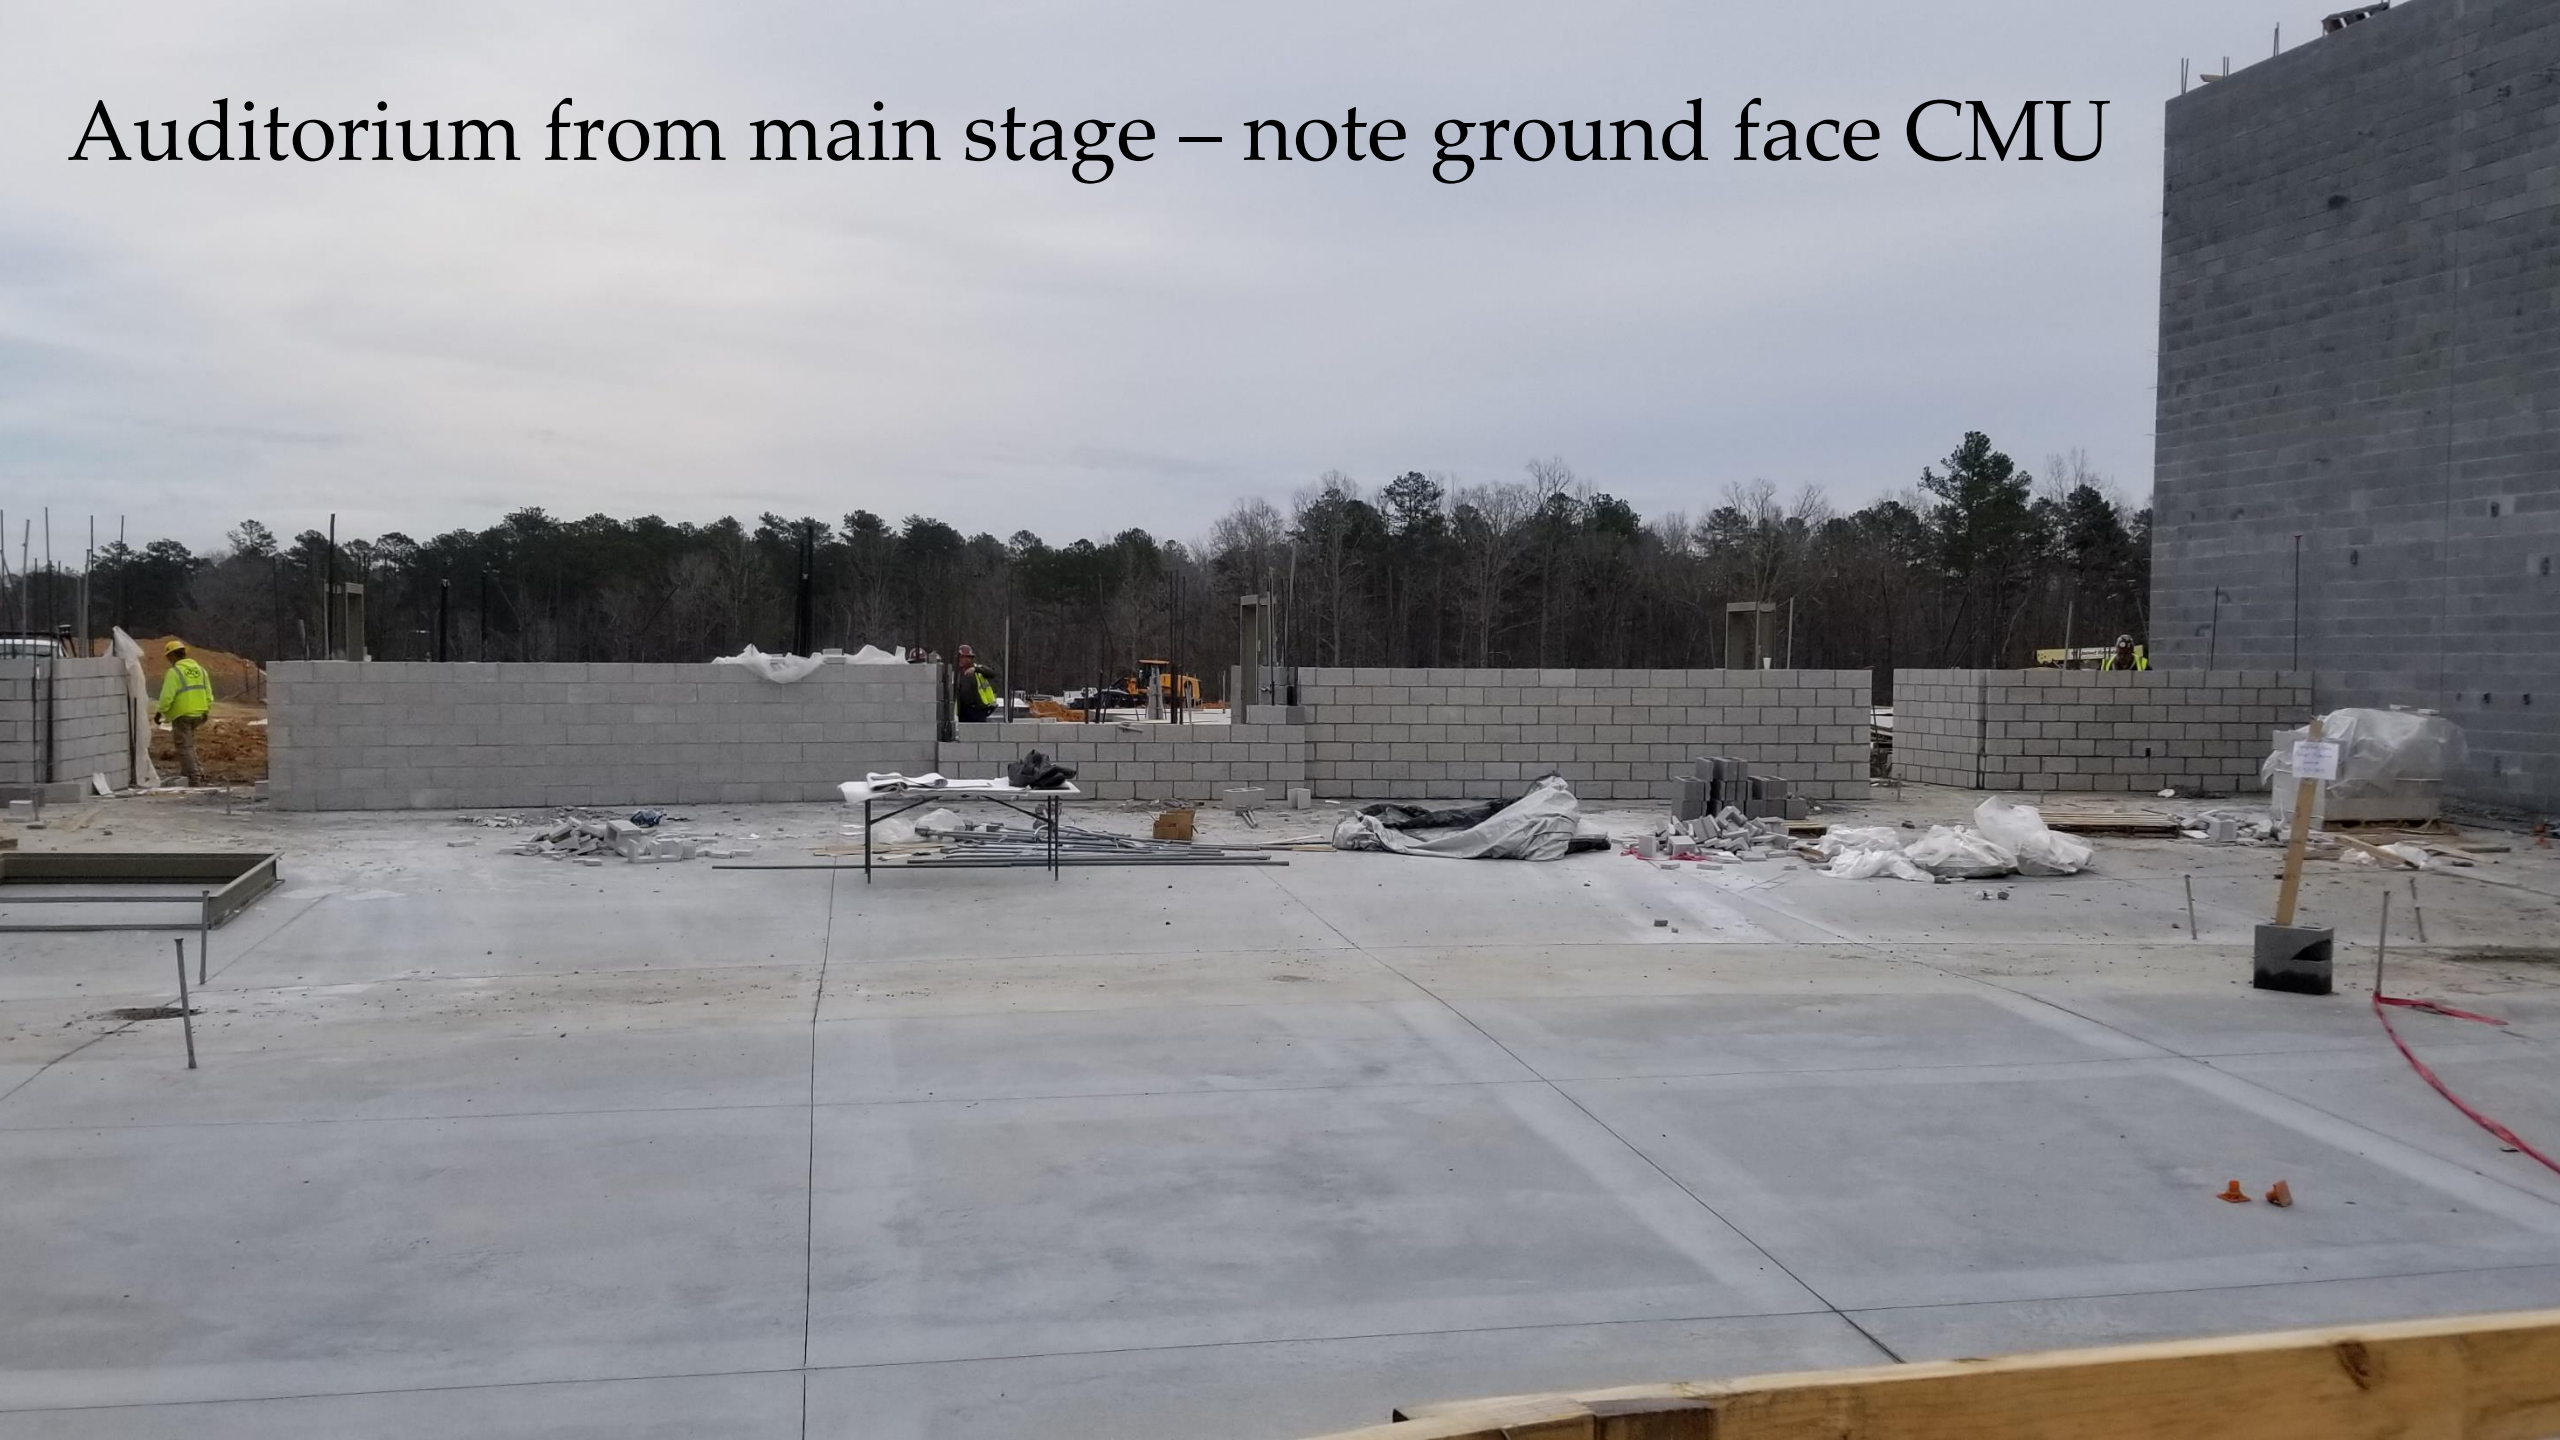

Main Gymnasium Roof Trusses



Auxiliary Gym Roof Trusses



Instructional Wing – Stairwell to Stairwell



Second Floor Roof Trusses



END – Questions?
