

# MCHS

Construction Project Update – December 3, 2018

# Construction Project Update

- Buildings

- CTE...The majority of the exterior CMU walls have been completed. Masons are now concentrating on the interior ground faced CMU walls to support roof trusses.
- CTE...Due to the rain, the schedule is now being adjusted and a new estimated substantial completion date will be presented at the next monthly meeting.
- HS...Contractor is now laying CMU walls for the gymnasiums. Some of Area A (weight room, locker rooms) floors have now been poured. The majority of the footers have been formed and poured.
- HS...the high school remains on schedule at this time.



# Construction Project Update

- Next 30 days
  - Complete the CMU walls necessary for structural steel.
  - Continue to pour slab on grade concrete floors for HS
  - Continue to install structural steel and decking at the CTE building.
  - Continue topsoil screening and placing top soil on athletic fields as sub-grade is completed.
  - Continue under slab utility work required for HS concrete floors to be poured.

Weight room/locker room floors being prepared





Lift required to build gymnasium walls installed





# Challenging site conditions





# CMU walls at front entrance/conference room





CMU walls being constructed at machine shop, HVAC






## Mezzanine and classroom – 1634 Welding





Second floor hallway leading to wood shop mezzanine

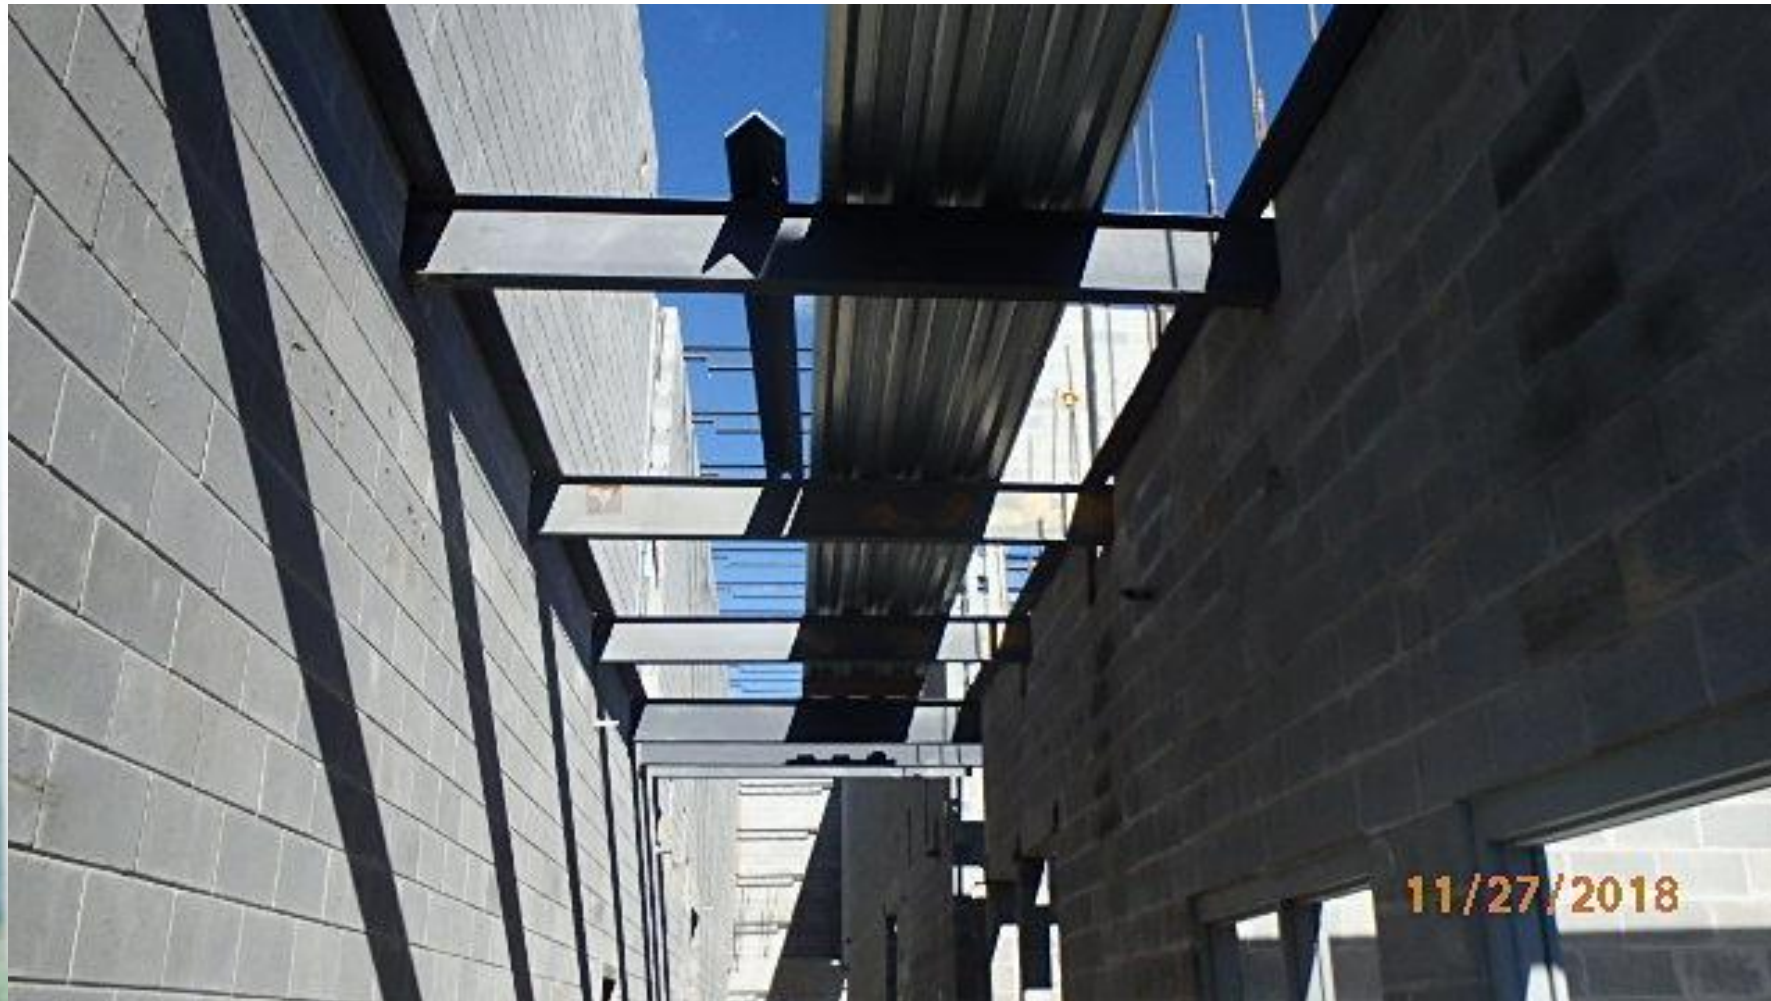



# Roof trusses being set at 1602 Construction Trades





Roof metal decking being laid at 1601 Wood Shop





Decking being welded to roof truss – 1601 Wood Shop

