

MCHS

CONSTRUCTION PROJECT UPDATE – JULY 8, 2019



CONSTRUCTION PROJECT UPDATE

- **BUILDINGS – COMPLETED LAST 30 DAYS**

- CTE...STAIRWELL TPO ROOF INSTALLED. CEILING GRID HAS BEGUN ON FIRST FLOOR. BLOCK FILL STILL IN PROGRESS. DRYWALL IS NOW BEING PRIMED. ROLL UP DOORS INSTALLED. COURTYARD CONCRETE HAS BEEN POURED. COURTYARD CANOPY WORK HAS BEGUN. MECHANICAL, ELECTRICAL, PLUMBING (MEP) STILL IN PROGRESS, GOAL IS TO ACHIEVE PERMANENT POWER AND HVAC STARTUP TO ALLOW FINISHES TO BE INSTALLED. DATA CABLE IS IN PROGRESS. FIRE ALARM IN PROGRESS.
- HS...TPO ROOF ON OFFICE AREA C IS AT 90%. EXTERIOR SHEATHING FOR AREA E IS IN PROGRESS, BRICK IN PROGRESS. CMU WALLS AT FRONT ENTRANCE AND CAFÉ IN PROGRESS. CMU WALLS SECOND FLOOR AREA E ARE COMPLETE. CMU WALLS FIRST FLOOR AREA F ARE AT 90%. CMU WALLS SECOND FLOOR AREA F ARE IN PROGRESS. SLAB ON DECK IS COMPLETE IN INSTRUCTIONAL WING, INCLUDING CONNECTOR.

CONSTRUCTION PROJECT UPDATE

- **NEXT 30 DAYS**

- CTE – MAIN GOAL WILL BE TO ACHIEVE PERMANENT POWER AND START HVAC UNITS TO ACHIEVE CONDITIONED SPACE. GAS TANK TO BE PLACED TO START BOILERS FOR DE-HUMIDIFICATION TO ALLOW FINISHES TO BE INSTALLED. ELEVATOR INSTALLATION WILL BE IN PROGRESS.
- HS – COMPLETE REPAIRS TO AREA B PIPE, PREPARE FOR SLAB POUR. INSTALL ROCK BASE IN MAIN CORRIDOR AREA. CONTINUE TO INSTALL METAL STUD WALLS IN INSTRUCTIONAL WING. SET HVAC EQUIPMENT ON MECHANICAL MEZZANINES. COMPLETE ROOF DECKING AREA D ONCE UNITS ARE SET. CONTINUE MEP INSTALLATION ALL AREAS. CONTINUE EXTERIOR SHEATHING, WEATHERPROOFING, AND BRICK VENEER.
- SITE –CONTINUE TO GRADING ROADWAYS AND PARKING LOTS. CONTINUE TO INSTALL ATHLETIC BUILDINGS.
- NEXT PROGRESS MEETING IS SCHEDULED FOR JULY 11, 2019 (ANOTHER ACADEMIC YEAR DOWN!).



CTE SUBSTANTIAL COMPLETION DATE – 11/05/2019


MCHS SUBSTANTIAL COMPLETION DATE – 3/11/2020

Scheduling meeting 6/26/2019 – Update following week.



Montgomery Central HS from Student Parking – Note Stone


KEY PLAN

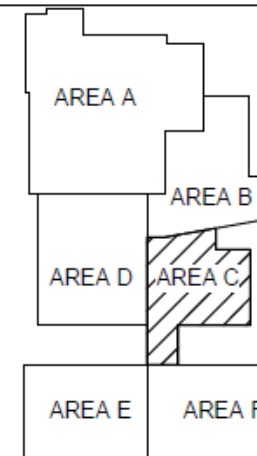




Main Entrance into Montgomery Central High School

KEY PLAN

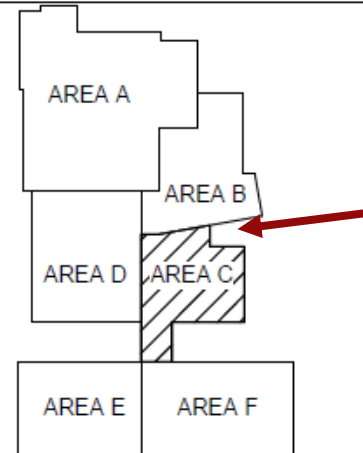



KEY PLAN

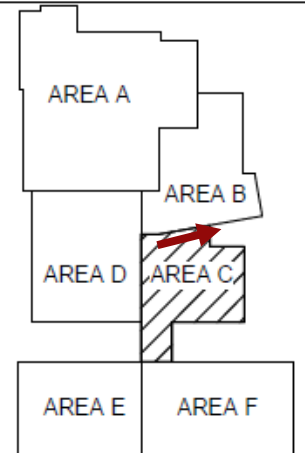


Main Entrance from Main Corridor – Display Cases Right



Gym Entrance Left – Café Sky Fold Door Right


KEY PLAN

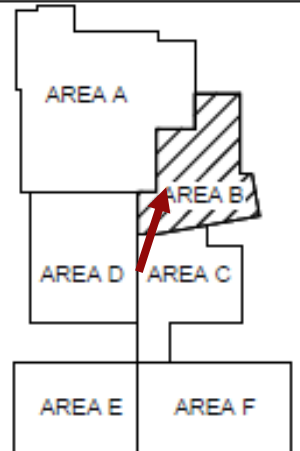



Main Corridor Looking South


KEY PLAN

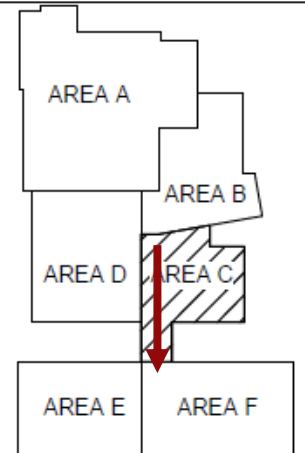



Main Lobby from Top of Steps


KEY PLAN

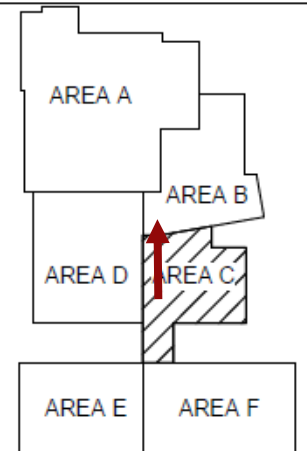



Second Floor Connector from F


KEY PLAN

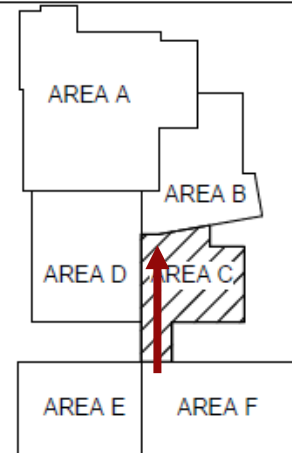



Second Floor Area F from Connector


KEY PLAN

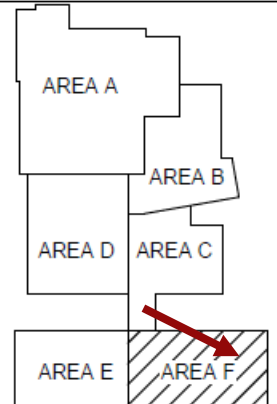



North Face of Instruction Wing Area F


KEY PLAN

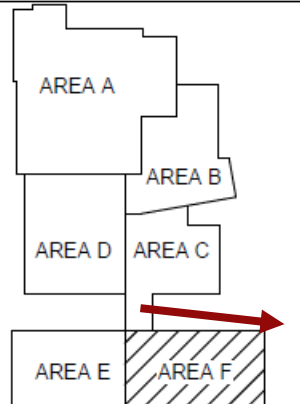



South Face of Area C - Office


KEY PLAN

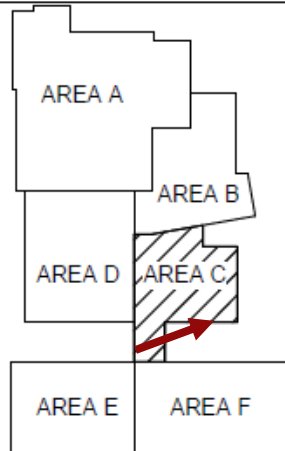



Courtyard between E and D


KEY PLAN

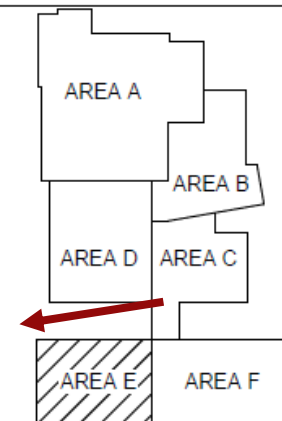



Area E Second Floor

KEY PLAN

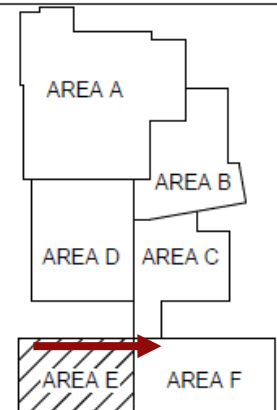



South – East Faces of CTE Building


KEY PLAN





CTE Rear Canopy in Construction


KEY PLAN





CTE Area 2 First Floor Corridor – Elevator Shaft Right


KEY PLAN





Culinary Arts from Student Station


KEY PLAN





Mr. Kern's Future Classroom and Mezzanine

KEY PLAN





Health Occupation Classroom – Second Floor


KEY PLAN













Main Elevator Second Floor

KEY PLAN





END SLIDE – QUESTIONS???

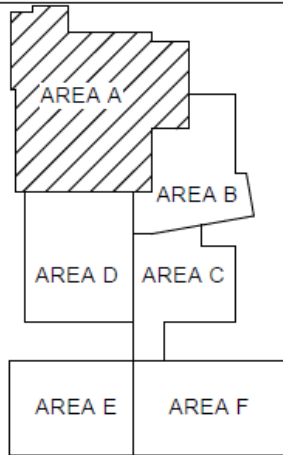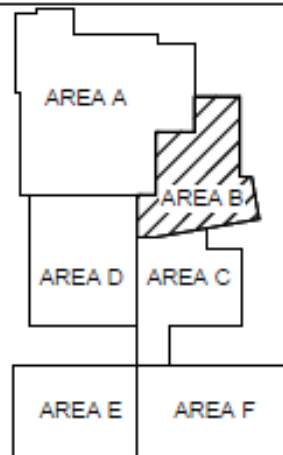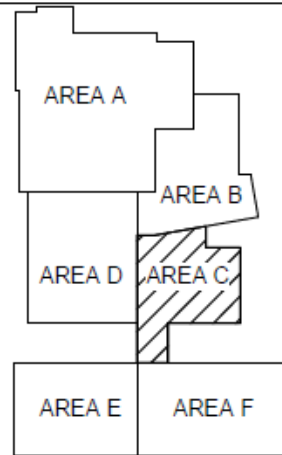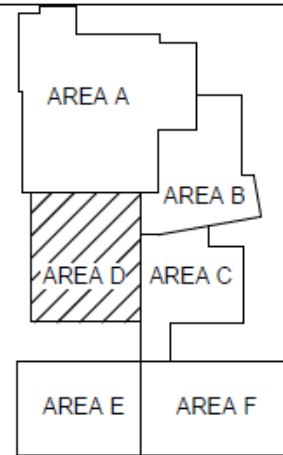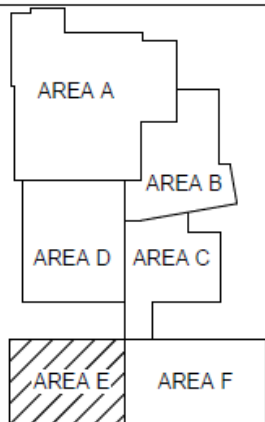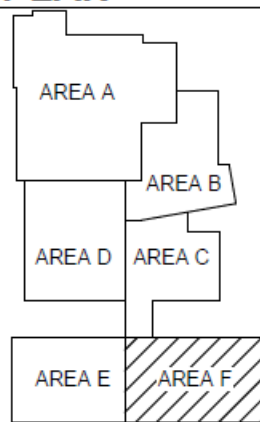KEY PLAN**KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN**

KEY BLOCK – DO NOT DELETE
